

Green Valliey Industries Limited

CIN NO.: U26942ML2007PLC008273

16th Jan 2026

No: GVIL/ENV/SC/2025-26/01

To,

The Additional Principal Chief Conservator of Forests (C),
Ministry of Environment, Forest and Climate Change,
Regional Office (NEZ),
Law-U-Sib, Lumbatngen, Near MTC Workshop,
Shillong, Meghalaya.

Sub: Status of Compliance of Environment Stipulations – Plant Regarding

Respected Sir/ Madam,

With reference to the subject cited above, please find herewith the status of compliance of Environment stipulations directed by SEIAA for the period April'2025 - September'2025

with details enclosed.

This is for your kind information and record please.

Yours Sincerely,

For Green Valliey Industries Limited.

Authorized Signatory
Pawan Kumar Joshi
(Vice President)



Enclosed:

- Status of Compliance Report for the period April'2025 - September'2025
- Ambient Air Monitoring Report. (Annexure-I)
- Stack Monitoring Report. (Annexure-II)
- Noise Level Monitoring Report. (Annexure-III)
- Fugitive Emission Monitoring Report (Annexure- IV)
- Work Zone Monitoring Report (V)
- Annexures as listed.

Copy to:

- The Member Secretary, State Environment Impact Assessment Authority, Shillong.
- The Member Secretary, Meghalaya State Pollution Control Board, Shillong.
- The Zonal Office, Central Pollution Control Board, Shillong.

Guwahati Office: 4th Floor, B Plaza, C.S. Road, Phangasari, Guwahati-781 005, T +91 361 2465481 / 82 / 83 / 84

Regd. Office & Plant: Vill. Nongsning, P.O. Chiehruphi, PS. Khliehriat, Dist. Jaintia Hills, Meghalaya-793 200

Group Corporate Office: 602 'LORDS' 7/1, Lord Sinha Road, Kolkata-700 071, T +91 33 22827367 / 7368 F +91 33 22828307

E : info@greenvalliey.com

A GNG GROUP COMPANY

Status of compliance of Environment stipulations as set by SEIAA for
M/S GREEN VALLIEY INDUSTRIES LTD.
for the period April '2025 – September '2025.

Introduction:- M/S Green Valliey Industries Limited was given environmental clearance for construction of an Integrated Cement Plant of 1300 TP D expandable to 2600 TPD along with 2x10 MW Captive Coal Based Thermal Power Plant at village Nongsning, Chiehruphi, Jaintia Hills, Meghalaya on 28th March, 2009.

STATUS OF COMPLIANCE OF ENVIRONMENT STIPULATIONS:

SPECIFIC CONDITIONS:

Sl. No.	Conditions	Status
1.	High efficiency Electrostatic precipitators (ESPs) shall be installed in the Thermal Power Plant to limit particulate emission to 50mg/Nm ³ .	Please note that the Thermal Power Plant for this site has not been installed yet.
2.	Dust extraction and suppression system along with water sprinklers shall be provided for controlling fugitive dust during transportation, in coal storage area and other vulnerable area of the plant.	- We have installed dust extraction and suppression system at all the transfer points. - We do use water spray on the transfer points of clinker cooler, preheater cyclone, Limestone crusher and Cement Mill to control dust emission in the plant. - At unloading points of coal, we have already installed water spraying system for effective dust suppression. - Water tanker is being used on regular basis for water sprinkling, from the main road to plant area.
3.	Water requirement shall be met from the existing water source which would be restricted to 1220 m ³ /day. No ground water shall be extracted for the DG set at any stage.	Water Consumption is below 1220 m³/day, for which we send the returns to MSPCB on monthly basis and No ground water is being extracted.
4.	Closed cycle cooling system with induced draft cooling towers shall be provided.	Please note that, the Thermal Power Plant for this site has not been installed yet.
5.	The treated effluents shall be re-circulated and reused within the plant area. There shall be no waste water discharge outside the plant boundary.	All the water used for plant operation are re-circulated and reused, through water cooling tower. STPs have been installed to treat domestic waste water



		and the treated water is being utilized for Plantation and sprinkling on roads.
6.	Rainwater harvesting shall be practiced. A detailed scheme for rain water harvesting to recharge the ground water aquifer shall be prepared in consultation with Central Ground water Authority/State Ground Water Board and a copy of the same shall be submitted within six months to the monitoring agency.	Rainwater harvesting have been set up and practiced, in consultation with Central Ground water Authority/ State Ground Water Board, (Annexure- 1).
7.	Leq of noise level in the DG set premises shall be limited to 75 db A and regular maintenance of equipment should be undertaken. For personnel working in high noise areas, personal protection devices should be provided. Acoustic hoods shall be provided in respect of all equipment's that have potential to contribute to noise pollution.	Personal protection devices are being used by all the workers working in high noise area of the plant and the noise produced are below the prescribed limit. (Attached Noise Monitoring Report as Annexure- III)
8	Dry ash collection system shall be provided in the Thermal Power Plant.100% ash utilization shall be insured from the very first day of commissioning of the thermal power plant.	We have not established Thermal power plant, hence no generation of Dry ash.
9.	A stack of minimum 100m height shall be provided with continuous on-line monitoring system in respect of Thermal Power Plant considering the dispersion sensitivity and geographical location of the plant. The data collected shall be analyzed and submitted regularly to the Meghalaya State Pollution control Board and SEIAA.	We have not commissioned Thermal Power Plant.
10.	The stack emission from various sources shall not exceed 50mg/Nm ³	The revised target of 30 mg/Nm³ is being followed strictly. The stacks have been connected to OCEMs which transmits online data to CPCB and MSPCB every 15 minutes. (Attached Stack Monitoring Report as Annexure-II).
11.	Bag house/ filters shall be provided to control the fugitive emissions during loading and unloading of raw materials/intermediate and finished products.	Bag house/ filters have been provided to control the fugitive emissions at vulnerable areas of the Plant. (Attached Fugitive Emission Monitoring Report as Annexure-IV)



12.	a) The Storage of the coal dumps shall be housed by permanent sheds open on all sides and stacked on impervious floor, preferably cemented to prevent Acid Mine Drain (AMD). b) The project proponent shall construct garland drains along with AMD Neutralisation tanks, in consultation with and approved by the SPCB c) No direct discharge of AMD into any drains/natural drains shall be allowed; proper treatment of AMD shall be done by the Project proponent.	• A permanent coal yard has been extended for its capacity and fully complied by concreting the floor with proper shed to avoid any contamination of water. • We have already constructed garland drains connecting to AMD tank, • We have approached MSPCB officials for upgrading and modifying our current AMD Tank for the design and their guidance (Annexure-2).
13.	The locations of ambient air quality monitoring stations shall be set up as per statutory requirement in consultation with the Meghalaya State Pollution Control Board (MSPCB) and additional stations shall be installed, in the downwind direction as well as where maximum ground level concentrations are anticipated.	• We have established four AAQMS in the plant as per the directions and guidelines of CPCB with the approval from MSPCB (Annexure- 3). at: • Near Guest house, • Near DM Plant. • Near Staff Colony. • 4- Near HOD Colony.
14.	Total water requirement shall not exceed 1220 m ³ /day. The project authorities shall install sewage treatment plant of minimum 80 m ³ /day capacity to treat domestic sewage and treated sewage shall be utilized for green belt development. No waste water shall be discharged outside the premises and zero discharge shall be ensured. Surface water restricted to a maximum of 1220 m ³ /day shall be drawn from perennial stream of Umtiling flowing nearby and no surface runoff from the factory premises shall either reach/contaminate Um-lunar or any other stream flowing at a site situated to the west of the industrial location.	• Daily water consumption is below the prescribed limit. • STPs have been installed for treating domestic sewage and the same treated water is being used in Sprinkling the road and Spraying for Plantation.
15.	The project proponent shall make all-out effort to use high calorific value hazardous waste in the kiln towards which necessary provision shall be made.	• We have approached Municipal Board of the District for Material use of High Calorific value hazardous waste (Annexure- 4). • However, waste generated within the Plant premises are being fed in the kiln.



16.	The project proponent have not proposed procurement/development of any captive mine in respect of limestone requirement which is estimable to be high. The project proponent shall take expedient steps to procure limestone's mining leases covering such mining area that would be necessary to sustain the limestone requirement of the cement plant. The entire process shall be completed by the time the industry becomes operational and the project proponent shall source its limestone's requirement to run its industry only from such mining leases. The project proponent shall compulsorily take all such steps as are necessary to discourage procurement of limestone that would tend to promote unscientific mining and consequential environmental degradation.	• Process for obtaining Prospecting License / Mining Lease for three blocks - Madan Pyrda Block –I (4.89 Ha.), Madan Pyrda Block –II (10.71 Ha.) & Surve Larung (44.58 Ha.) has already been taken prior to the industry became operational. • Present status of all the three applications are as follows: - 1. <u>Madan Pyrda Block –I (4.89 Ha.)</u> – Mining Plan has been Approved. EC granted; Final Approval for Forest Clearance has been obtained. Mining Lease Deed has been executed. 2. <u>Madan Pyrda Block –II (10.71 Ha.)</u> - ORDER / LOI (Letter of Intent) obtained. The Mining Plan has been approved. EC granted. All other clearances such as Forest Clearance, are in progress. 3. <u>Surve - Larung (44.58 Ha.)</u> – ORDER / LOI (Letter of Intent) obtained. The Mining Plan has been approved. All other clearances such as Forest Clearance, EC etc. are in progress.
17.	The project proponent shall transport raw materials and industrial products through covered means.	• All raw materials and industrial products are transported through covered means.
18.	The project proponent shall secure a certificate from the Principal Conservator of Forests, Meghalaya that the core project area is a non-forest land within 3 months of issue of prior Environmental clearance.	• Securing of Non – Forest Certificate for the core project area from Principal Conservator of Forest, Meghalaya is under process.
19.	Thirty three percent of the core project area (17ha) shall be developed as green belt as per the guidelines of central pollution control board to mitigate the effects of fugitive emission. The program ought to be completed within 5 years from the date of issue of prior Environmental Clearance adhering to time and cost schedule detailed by the project proponent through incurring and expenditure of Rs. 9.5 Lakhs as stated by him.	• The company has developed 15.69 Ha as green belt and remaining plantation work is in progress. (Annexure- 5)



20.	The project proponent shall provide a Health care Center with all emergency medicines and ambulance along with full time doctors. There shall be a casualty ward that would be operational round the clock duly attended by a suitable doctor. Occupational health surveillance of the workers shall be carried out on a regular basis in terms of their EMP document and records shall be maintained as per the Factories Act.	• Occupational Health Care Centre already functioning with company appointed Medical Officer, accompanied by trained lab technician, nurse and helper. Health register is being maintained. • We also have Ambulance facility to commute and address employees with any severe medical issues. • Occupational Health surveillance of employees are carried out annually in consultation and check up with experts for which we maintain the record.
21.	Measures shall be taken to prevent impact of particulate emission/fugitive emission, if any, from the proposed plant on the surrounding private forest areas depicted in their land use study.	• Measures are taken to prevent impact of particulate emission/fugitive emission, if any, from the proposed plant on the surrounding private forest areas depicted in their land use study.
22.	The project proponent shall raise conservation plots (over an area not less than 2ha) complete with green house, mist chamber etc. in respect of plants of conservation value in consultation with Botanical survey of India complete with cost and activity schedule within 6 months from the date of issue of prior Environmental Clearance and initiate implementation immediately thereafter. A copy of the conceptual shall be submitted to the monitoring agency.	• Mist Chamber constructed (under the consultation with Botanical Survey of India, Shillong). Further development and upgradation in progress. (Attached photograph as Annexure-6)
23.	The project proponent shall sponsor research and development for conservation of threatened category of species occurring locally such as <i>Nepenthes khasiana</i> and <i>Calamus khasiana</i> to be carried out by an appropriate research or academic institution located in Meghalaya within a year of issue of prior Environmental Clearance. The research project shall be instituted at an expenditure of a minimum of Rs. 5 lakhs per year spread over at least 3 years.	• Will be done.
24.	A plan for conservation of wild fauna in consultation with a reputed institution such as Wildlife Institute of India, Dehradun shall be prepared and implemented. Such conservation plan drawn in respect of wildlife would be submitted to the monitoring agency within a maximum of 1 year from the date of issue of prior Environmental Clearance.	• As per discussion in MoEF&CC Office, we are already a part of the combined Wildlife Conservation Plan for Narpuh Circle.



25.	A sum of Rs. 2302 lakhs (being 9% of capital cost of infrastructure of the project) shall be spent by the project proponent towards environment protection. A further sum of Rs. 15 lakhs per year shall be spent by the project proponent towards economic development of the area till the project subsists.	We are playing our part in support towards economic development of the area, attached expenditures in previous 3 Financial Years. (Annexure- 7)
26.	The pollution control units/processes to be installed shall be vetted by experts from a reputed institute such as NEERI, IIT and NIT.	The installed pollution control units/processes have been vetted by experts from NIT (Annexure- 8)
27.	The project proponent shall ensure monitoring of biodiversity component at the interval of every five years by an independent expert agency to assess the impact of the project thereupon. The report shall be submitted to the monitoring agency.	Discussed with the experts from Centre for Biodiversity and natural resources conservation, Assam University for their guidance and help in this matter. We have also approached SEIAA for their intervention and guidance. (Annexure- 9)

GENERAL CONDITIONS:

Sl. No	Conditions	Status
1.	The project proponent shall not violate applicable provisions of any Acts, Rules Orders of the Government and judicial orders issued by the Hon'bl Supreme Court/ High Courts/ NGT, applicable to the project.	GVIL is abiding by the provisions and shall continue to do so.
2.	No further expansion or modification in the plant shall be carried out without prior approval of the Ministry of Environment and Forests or their nominated authority as the case may be. In case of deviation or alteration in the project proposal from those submitted to this committee for clearance a fresh reference shall be made to the SEAC through SEIAA to assess the adequacy of conditions imposed and to add additional environmental protection measures required, if any.	GVIL will follow the guidelines.
3.	The gaseous emissions (SO ₂ , NO _x) and particulate matter from various process units shall conform to the standards prescribed by the concerned authorities from time to time. At no point of time, the emissions shall exceed the prescribed limits. Interlocking system of equipment shall be chosen such that in the event of failure of any pollution control system adopted by the unit, the unit shall be immediately put out of operation and shall not be restarted until the desired efficiency has been achieved.	We have installed online SO₂, NO_x analyzers and are maintaining the emission under prescribed limit and online data is being submitted to MSPCB and CPCB on regular basis.




4.	The industry shall undertake the following waste minimization measures: • Reuse of by-products from the process as raw materials or as raw material substitutes in other processes. • Use of closed pneumatic system for transport of fine material. • All venting systems shall be connected with dust or particulate arresting equipments. • Dust/particulate matter collected in pollution control equipments shall be reused.	• There is no generation of any by-products at our Plant • We are using Air Slides to transport fine materials, which consume less power, has no dust loss and is a closed system. • RABH and ESP have been installed connecting Cooler, and other venting lines. • Dust/ particulate matter collected in pollution control equipments are being reused.
5.	Fugitive emissions in the work zone environment, product and raw materials storage area shall be regularly monitored. The emissions shall conform to the limits imposed by the SPCB/CPCB.	• Fugitive emission tests and Work Zone Monitoring are being carried out, which conforms to the limits imposed by SPCB/ CPCB. Attached as (Annexure- IV and V).
6.	The overall noise levels in and around the plant area shall be kept well within the standards by providing noise control measures such as acoustic hoods, silencers, enclosures etc. on all sources of noise generation. The ambient noise levels shall conform to the standards prescribed under the Environment (Protection) Act, 1986, Environment (Protection) Rules, 1989 viz. 75 dBA (daytime) and 70 dBA (night time)	• Acoustic hoods, Silencers have been provided and the noise level is being maintained under the prescribed limit.
7.	The project authorities shall strictly comply with the rules and guidelines under Manufacture, Storage and Import of Hazardous Chemical Rules, 1989 as amended and Hazardous Waste (Management Handling) Rules, 1989 as amended from time to time. Authorization from the MSPCB shall be obtained for collection, treatment, storage and disposal of hazardous wastes.	• Complied. Authorization from the MSPCB has been obtained for collection, storage and disposal of hazardous wastes, attached as (Annexure- 10), and Other Waste (Annexure- 11).
8.	Rainwater harvesting measures shall be done within the premises. Ground water recharge structures shall be installed around the plant area in consultation with local authorities to maintain the ground water table.	• Complied. Rainwater harvesting and ground water recharge structures have been set up and practiced, in consultation with Central Ground water Authority/ State Ground Water Board, (Annexure- 1).



9.	The company shall undertake eco-development measures including community welfare measures in the project area for the overall improvement of the environment. The eco- development plan should be submitted to the monitoring agency. Within six months of issue of prior Environment clearance.	The eco development plan has been approved by NEHU. Has been all rules and Regulations it will be followed by Green valley Industry LTD.
10.	A separate Environmental management cell equipped with full-fledged laboratory facilities as detailed by the project proponent shall be set up to carry out the Environmental Management and monitoring functions	We have established full-fledged Environmental Laboratory as per your guidelines.
11.	All pollution control equipment in STP shall be manned full time by trained personnel.	STP is functional and being operated by trained personnel.
12.	The implementation of the project vis-a-vis environmental action plans shall be monitored by the Regional office, Ministry of Environment & Forest duly assisted by the SPCBA six monthly status report shall be submitted to the stated institutions and state Environment impact Assessment Authority/SEAC apart from posting the same on the website of the company.	- A six-monthly status report is being submitted to MoEF&CC, Shillong. - The same is updated and posted on our official website at: http://www.maxcement.co.in/
13.	The project proponent will make provisions to keep standby spares at the plant site of pollution control units/devices during operation of the cement plant.	We maintain spares for Reverse Air Bag House and also spares for Filter Bags of other sections.
14.	The project proponent will arrange to carry out regular maintenance of all the pollution control Units/devices to ensure its sufficient performance all the time.	Our maintenance team is regularly monitoring the pollution control devices to keep the pollution control equipment in good condition and ensure efficient performance at all times.
15.	The Project proponent shall not violate applicable provisions of any Acts, Rules Orders of the Government and Judicial orders issued by the Hon'ble Supreme court/ High courts/NGT, applicable to the project.	We shall abide by any Acts, Rules Orders of the Government and Judicial orders issued by the Hon'ble Supreme court/ High courts/ NGT, applicable to the project.



Annexure -1

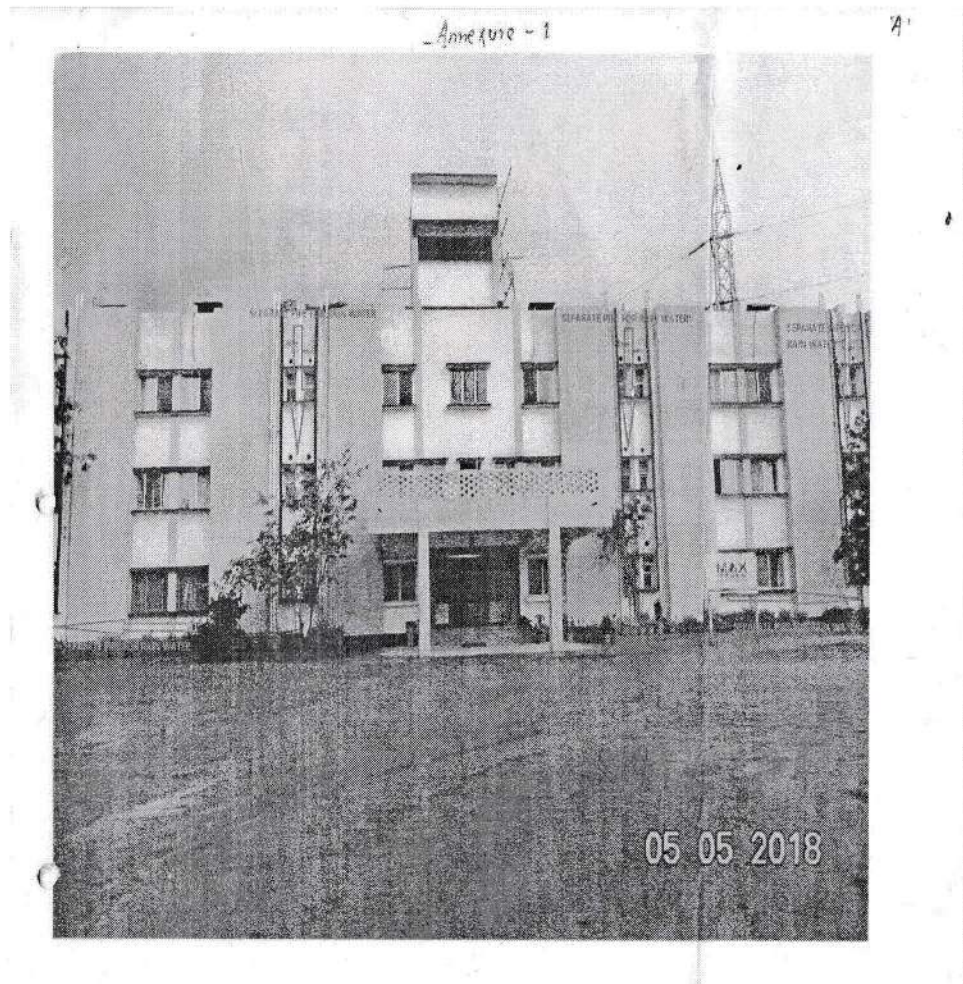

Ground Level Recharge for Rain Water

A Ground level recharge plan is implemented for non-polluted rain water in our Guest House building near Administration office for the roof top area to recharge the ground level through separate PVC pipes of 8 inch dia. Whereas, before the onset of the monsoon all the catchment area (roof top) considered for recharge is cleaned to avoid any contamination. A mesh/Jali is provided at the inlets to roof rain water pipes so that leaves or any other solid waste/debris is prevented from entering the recharge pit. An overflow pipe is provided in recharge chamber(s) to route the extra water.

Based on site condition length and breadth of the recharge chamber is designed keeping its volumetric capacity as per requirement and RCC slab thickness and reinforcement is dependent on structural loads. Thickness of recharge chamber walls is 0.2 meter and its depth is 1.6 meter. Filter media of 1.1 meter thickness is in four layers comprising of 0.4 meter thick layer of boulders (50-200mm) at the bottom, 0.3 meter thick layer of gravels (5-10mm) in the middle and 0.3 meter thick layer of coarse sand (1.5-2.0mm) is at the top so that the silt content that will come with runoff will be deposited on the top and can easily be removed and 0.1 meter thick protective layer of pea gravels will be provided over the coarse sand layer of the filter media.

Moreover, recharge Chambers is cleaned before onset of monsoon season every year including removal, washing and relaying with topping up of the pea gravel and filter media layers whereas recharge chambers is checked and cleaned for smooth operation.




(6)

Annexure - 2

Green Valley Industries Limited

Location - Guest House

(N-25°14'21.2" E-92°23'15.9")MSL-693M

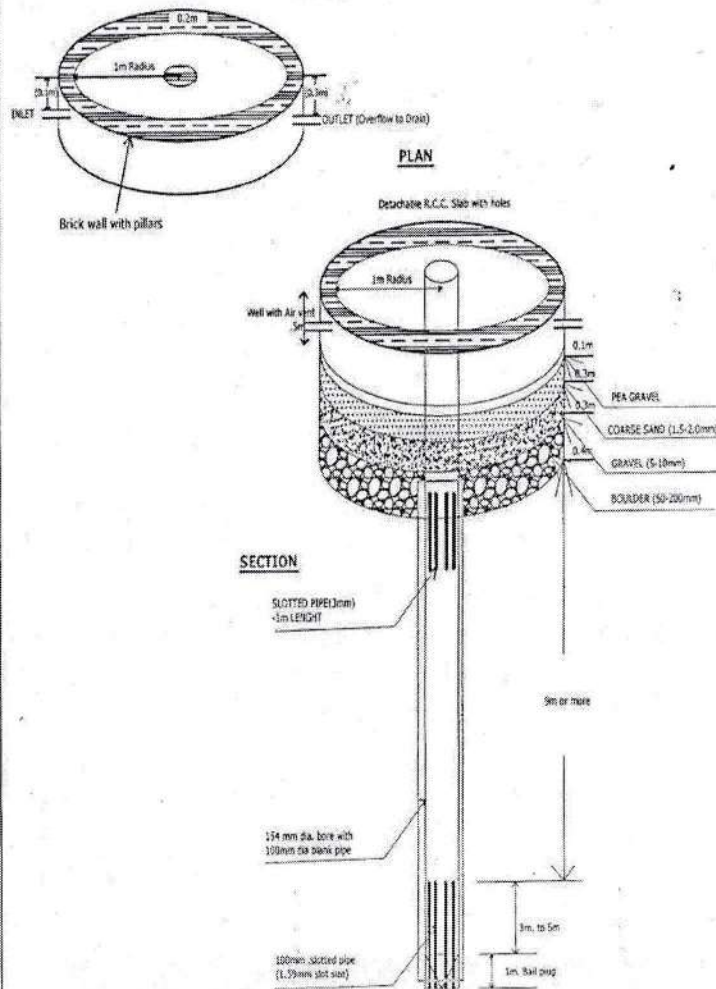Rain Water Harvesting / Ground Level Recharge
(Roof top area up to 470sq.m)

Annexure-2

Green Valliey Industries Limited

AMD TANK



Annexurer-3

Meghalaya State Pollution Control Board
Forests & Environment Department, Government of Meghalaya
"ARDEN" Lumpyngngad, Shillong - 793014
Website : <http://megspcb.gov.in>



No. MPCB/CL-9(A-III) /2024-2025/ 141

Dated Shillong the, 2nd August 2024

To,

Sr. Pawan Kumar Joshi,
Asst. Vice-President,
Green Valley Industries Ltd.,
Nongsting,
East Jaintia Hills District,
Meghalaya

Recd on
dt. 17.8.24
31

Sub: Setting up of AQM stations-reg

Ref: Your letter No. GVI/ENV/MSPCB/2024-25/01 dated 4th July 2024

Sir,

With reference to the above, I am to inform you that the Board has no objection for setting up of AQM stations in your plant premises as per details stated below:

Sl.No.	Location	Co-ordinates
1.	Near Guest House	N-25°14'22.5" / E-92°23'16.0"
2.	Near Staff Colony	N-25°14'33.5" / E-92°23'27.1"
3.	Near Old DM Plant	N-25°14'15.5" / E-92°23'57.5"
4.	Near HOD Colony	N-25°14'19.6" / E-92°23'18.0"

This is for your information and needful.

Yours faithfully

(Dr. G.H. CHYRMANG, MFS)
MEMBER SECRETARY
MSPCB, SHILLONG

No. MPCB/CL-9(A-III) /2024-2025/

Dated Shillong the, 2nd August 2024

Copy to:-

1. The Regional Office, MoEF & CC, RFR, Shillong, for favour of information,
e-mail: msofr-shillong@env.in
2. The Regional Director, Regional Directorate Shillong, Central Pollution Control Board, for information,
e-mail: regshillong.msofr@env.in

MEMBER SECRETARY
MSPCB, SHILLONG

Contact details : Email : memsecy.spcb-meg@gov.in, megspcb@rediffmail.com; Telephone Numbers : Chairman-8384-2521217; Member Secretary-2522832;
Scientific-2521754; Engineering-2521833; Legal-2521044; Laboratory-2521720; Administration-2520073; Accounts-2522124; Telefax-2521754



Annexure-4

Green Valley Industries Limited

CIN NO.: U26942ML2007PLC008273

No: GVIL/2017-18/TNV/42

14th September, 2017

To,

The Chairman,
Meghalaya Pollution Control Board
ARDEN, LUMPYNGAD, Shillong-793014,
Meghalaya.

Subject- Direction as empowered under section 5 of the Environment (prevention) Act, 1986.

Ref, No.MSPCB/LEGAL-93/2017/2017-18/35

Dear Sir,

With reference to letter subject cited above, we would like to inform you that we have approached to the entire concerned agency for providing us information on Refused Derived Fuel (RDF) with High calorific waste for our industries as feeding element, within the 100 KM area of the plant location.

This is for your information and record please.

Thanking You,

For Green Valley Industries Ltd.

Pawan Kumar Joshi

General Manager

Enclosure: Letter copy



Guwahati Office : 4th Floor, LB Plaza, G. S. Road, Bhargaguri, Guwahati - 781 005, T +91 361 2465481 / 82 / 85 / 84
Regd. Office and Plant : Vill. Nongning, P.O. Chiehnphi, PS. Khiehnat, Dist. Jaintia Hills, Meghalaya - 796 200
Group Corporate Office : 602 LORDS' 7/1 Lord Sinha Road, Kolkata - 700 071, T +91 33 22827367 / 7368, F +91 33 22828007
E : info@greenvalley.com

A GNG GROUP COMPANY



Annexure-5

Green Valley Industries Limited

CIN NO.: U26942ML2007PLC008273

Plantation Details at GVIL.

Location	Plantation area
Colony	54861.00 m ²
Old Magazine	2464.00 m ²
Airain Block	174.00 m ²
Behind CCR	230.00 m ²
HOD Block	90333.00 m ²
Behind Crusher	-----
Total Area (2017)	148062.00 m² = 14.81 ha
WED Plantation 5th June 2019:	
Behind Er. Block	427.00 m ² = 0.043 ha
WED Plantation 5th June 2020:	
Near Pump house	241.43 m ² = 0.024 Ha
Founder's Day (13th August 2020) & Independence Day (15th Aug 2020):	
Near NH-6, HOD Road, near Airtel Tower and New Village road	1995.909 m ² = 0.4 Ha
Founder's Day (13th August 2021):	
Near Truck Parking lot	1136.500 m ² = 0.12 Ha
WED Plantation 5th June'22 & Founder's Day (13th Aug'22):	
Behind New Store, Temple and G+1 Building	246.738 m ² = 0.02 Ha
WED Plantation 2023:	
Near HOD Park and Temple area	378.695 m ² = 0.04 Ha
WED Plantation 2024 (5th June'24) & Founder's Day (13th Aug'24):	
Near Raw Mill and behind Guest House	1105.77 m ² = 0.11 Ha
WED Plantation 2024 (5th June'25):	
HOD Colony near Triveni Block	1240.40 m ² = 0.12 Ha
Total Plantation Area	15.69 Ha

Updated by,


Lohu Edelfrill,
Env. Sr. Executive

Verified by,


Kamal Kanta Sahoo,
Manager




Gowahati Office: 4th Floor, LB Plaza, G.S. Road, Bhangagarh, Guwahati-781 005, T +91 361 2465461 / 62 / 83 / 84
Regd. Office & Plant: Vill. Nongsnang, P.O. Chichruphi, PS. Khichriat, Dist. Jaintia Hills, Meghalaya-793 200
Group Corporate Office: 602 LORDS' 7/1, Lord Sinha Road, Kolkata 700 071, T +91 33 22827367 / 7368 F +91 33 22828307
E : info@greenvalley.com

A GNG GROUP COMPANY



Annexure-6

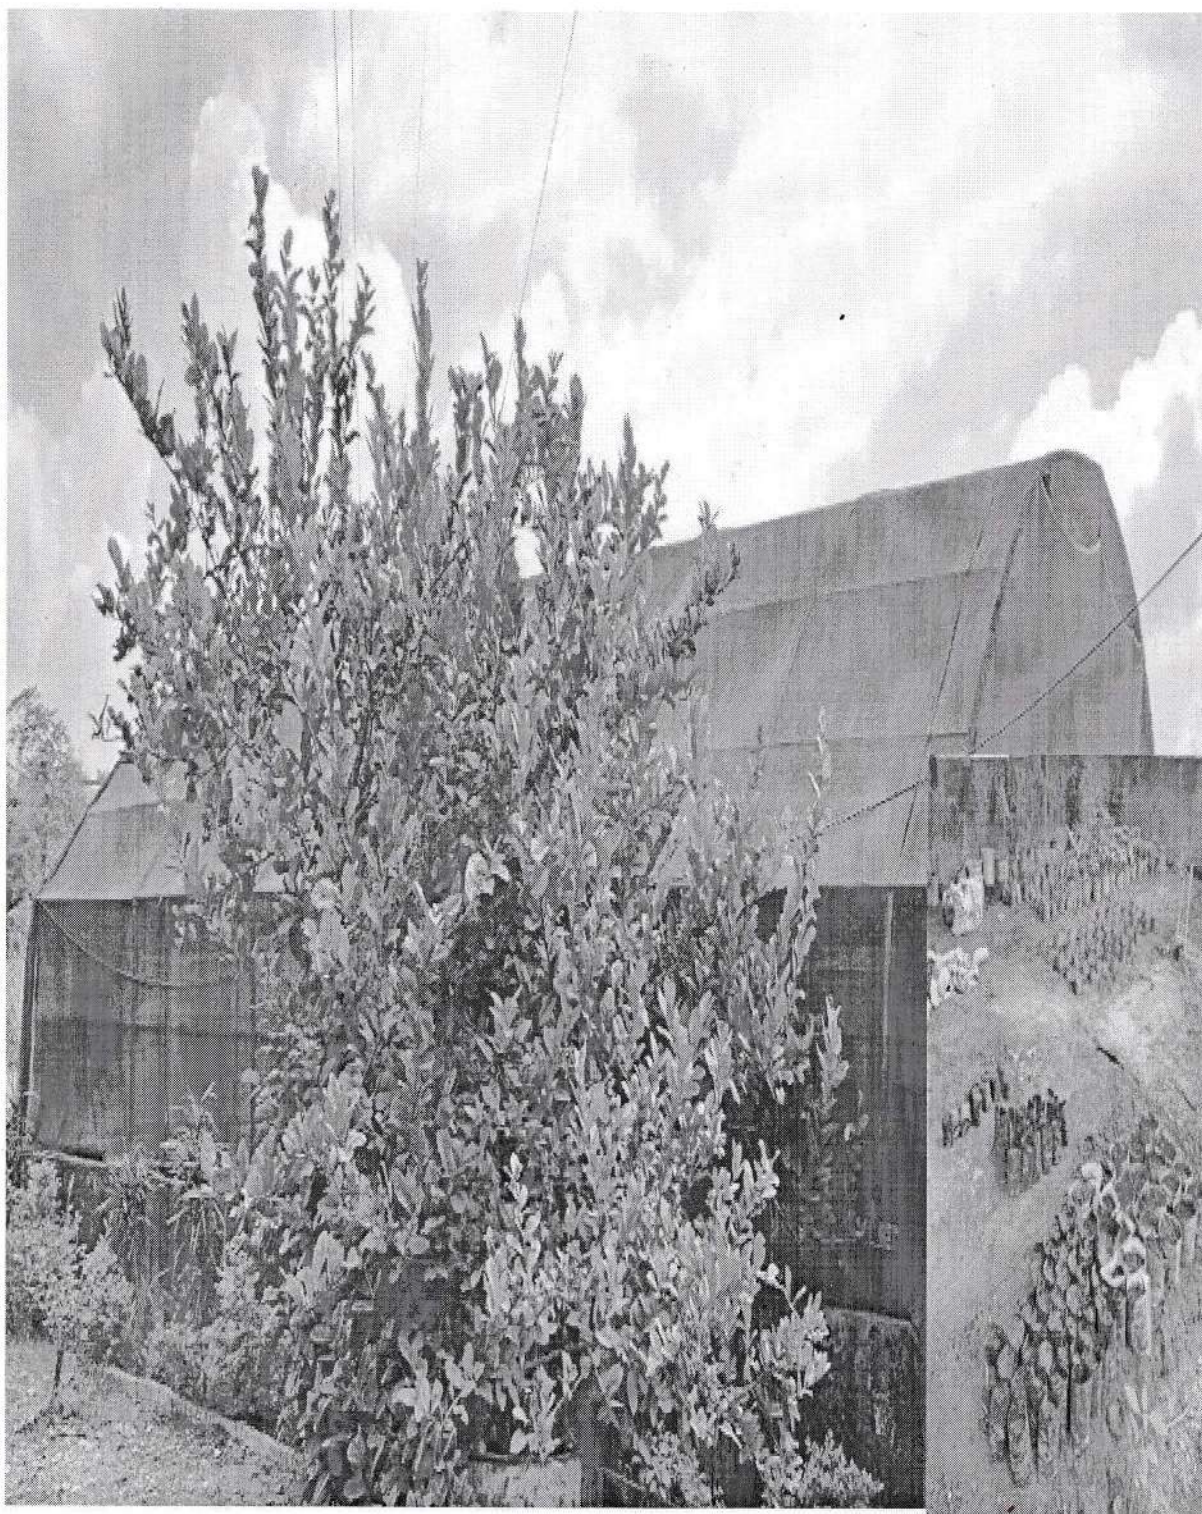

Annexure-7

Expenditure incurred for Socio-Economic Development F.Y. 2021-22

PAID ON A/C OF	AMOUNT (RS.)
Elaka Sutnga	5,62,500
Nongsning Village	4,07,203
Chiehruphi Village	54,729
Lumshnong Village	1,00,000
Elaka Narpuh	50,000
Nongsning Village U.P. School	1,00,000
Garo Union Sec. School	1,00,000
Dustbin for Byndihati Village	1,20,000
Water Supply at Village	1,30,000
Const. of Boundary Wall at Sutnga Market	4,78,000
Plantation for Founders Day	62,050
Grocery for Child Orphan Home	38,548
Police Dept. Shillong for 8 Mojos	42,000
TOTAL	22,45,030

F.Y. 2022-23

PAID ON A/C OF	AMOUNT (RS.)
Elaka Sutnga	5,00,000
Nongsning Village Development	4,07,203
Lumshnong Village Development	1,00,000
Chiehruphi Village Development	54,729
Elaka Narpuh Village Development	50,000
Amount paid to Director for remuneration	1,50,000
North East India Mission Association	1,00,238
Music & Singing Committee Wahiajer Narpuh	10,000
Stipend for Mines work	8,000
Kyrmen Wahlang	1,50,000
Sutnga Sports Social & Cultural	25,000
Appreciation of Subroto Cup Runner's up, from RC Eve School	33,525
Developing playground for Sutnga Sports & Games	75,000
Fete for Nongsning Village	5,000
Const. of wall for Thyndai Child care Inst Cum counselling Care	2,50,000
Lumshnong Village development work	5,02,351
Financial assistance for self-employment generation	20,000
Donation of CGI sheets at Nongsning Vill. Due to Cyclonic Storm	31,850
TOTAL	24,72,896

F.Y. 2023-24

PAID ON A/C OF	AMOUNT (RS.)
Elaka Sutnga	5,25,000*
Nongsning Village Development	4,21,576*
Lumshnong Village Development	1,00,000*
Chiehruphi Village Development	56,465*
Elaka Narpuh Village Development	50,000*
Annual remuneration Nongsning vill U.P. School	1,00,000*
Water Supply at Village	1,30,000*
Financial assistance to Dorbar Shnong Nongsning	3,00,000
Sutnga Sports Social & Cultural Club	60,000
Meghalaya State Pollution Control Board on account of River rejuvenation.	3,00,000
Contribution of car stickers & jute pencil bags to MoEF&CC	62,776
Financial Support to 34th Grand Lympung of Seng Khihlang, Wahiajer	20,000
Sponsorship for 9th Sprint Challenge, EJAMSA	72,260
Construction of football field building at Chiehruphi	5,00,000
TOTAL	26,98,077



Paid On A/C Of	Amount (RS)
Sutnga Sports Social and Cultural Club	75,000
Office of Dorbar Shnong Chiehruphi	30,000
Social Welfare Organisation Nongsning	40,000
Office of the Medical & Health Officer I/C Sutnga CHC, East Jaintia Hills, District	3,25,966
Dong Umshoo Lumshnong	3,00,000
Dong Umshoo Lumshnong	4,00,000
Sutnga Sports Social and Cultural Club	
Total	11,70,996





DEPARTMENT OF CIVIL ENGINEERING
NATIONAL INSTITUTE OF TECHNOLOGY SILCHAR

(An Institute of National Importance)

CECON THE CONSULTANCY CELL

P.O. - Silchar-788 010, Cachar (Assam) FAX 03842-224797 Telephone (HOD) 03842-242910

No. CECON/2018/60/F-2/43

Dated Silchar 09.05.2018

Ref. Letter No. Nil Dated 07.3.2018

**Vetting Report of Pollution Control Unit at Max Cement plant,
Green Valley Industries Ltd. at village Nongsning, East Jaintia Hills, Meghalaya**

A team from NIT Silchar visited the Max Cement plant, Green Valley Industries Ltd. at village Nongsning, East Jaintia Hills, Meghalaya for the physical inspection for the pollution control units installed at the cement plant on 24th March 2018.

It was physically observed that all the pollution control bag filter bags installed in Coal Mill, Cement Mill, LS Crusher and Packing plant sections were functioning properly whereas the two major pollution control units required for Cement Plant specifically Electrostatic Precipitator (ESP) and Reverse Air Baghouse (RABH) were operating successfully.

Both ESP and RABH are supplied by Thermax Ltd. (Enviro Division), Pune and installed by Waichandnagar Industries Ltd. in the year 2008 – 2009.

The specification and capacity of Pollution Control devices is sufficient for arresting dust as per the design capacity of the Mills in the reference to manual.

(Dr Upendra Kumar)

MIE, FICER
MCE (Jadavpur University), PhD IIT Kharagpur
Specialization: Environmental Engineering
Associate Professor & Head of Department
Department of Civil Engineering,
National Institute of Technology Silchar
NIT Silchar-788010, Cachar, Assam

Head of the Department
Civil Engineering,
NIT Silchar- 10

Testing of Civil Engineering Materials, Earthquake Resistant Design of Structures, Proof checking, DPM preparation, Flood Mitigation measures, Site Soil Exploration, Slope Stability, Pavement Design, Contour Maps, Site Survey, Waste Management.



Annexure-9

Green Vallley Industries Limited

CIN NO.: U26942ML2007PLC006273

Date: 18th June, 2024

No: GVIL/INV/SEIAA/SC/2024-23/01

To,

The Chairman,
State Environment Impact Assessment Authority,
Silva Lure Building, Lower Lachumiera,
Shillong- 793001

Subject: Compliance of Environmental Conditions- for your intervention

Dear Sir,


As per the subject, and the conditions under our EC No. SEIAA/PROJECT-1/2007, dated Shillong, the 28th March, 2009, we request for your intervention in certain changes in conditions as stated below:

- a) The points under Specific Condition No. XXVII, which states, "The project proponent shall ensure monitoring of biodiversity component at the interval of every five years by an independent expert agency to assess the impact of the project thereupon. The report shall be submitted to the monitoring agency." We have approached Wildlife Institute of India but have not received a proper response, thus requesting your kind office to suggest a compatible party from whom we can carry out the said condition or if modifications can be made to comply with the same.
- b) General Condition No. ix stating, "The company shall undertake eco-development measures including community welfare measures in the project area for the overall improvement of the environment. The eco-development plan should be submitted to the monitoring agency within six months of issue of prior Environment clearance." We seek guidance and advice from your kind office to suggest a compatible party from whom we can carry out the said condition to comply with the same.

We look forward to your kind guidance and advice for the above mentioned conditions. Thanking you for your unwavering support at all times.

Yours Sincerely,

For Green Vallley Industries Limited,


Authorized Signatory
Pawan Kumar Joshi
(Asst. Vice President)



Enclosed: EC copy, EC No. SEIAA/PROJECT-1/2007, dated Shillong, the 28th March 2009.



Guwahati Office: 4th Floor, LB Plaza, G.S. Road, Bhangagarh, Guwahati 781 005, T +91 361 2485461 / 82 / 83 / 84
Regd. Office & Plant: Vill. Nongshing, P.O. Chiehruph, P.S. Kalierniat, Dist. Jaintia Hills, Meghalaya-793 200
Group Corporate Office: 602 'LORDS' 7/1, Lord Sinha Road, Kolkata-700 071, T +91 33 22827367 / 7368 F +91 33 22828307
E : info@greenvallley.com

A GNG GROUP COMPANY



Annexure-10



(24)
Meghalaya State Pollution Control Board
Forests & Environment Department, Government of Meghalaya
'ARDEN' Lumpyngngad, Shillong-793014
Website: <http://megpcb.gov.in>



No. MPCB/ATH-34/2011/2021-2022-24

Dated Shillong, the 4th Feb, 2022

FORM - 2
[See Rule 6(2)]

FORM FOR GRANT/RENEWAL OF AUTHORIZATION BY MEGHALAYA STATE POLLUTION CONTROL BOARD, SHILLONG FOR OCCUPIERS, REPROCESSORS, REUSERS AND OPERATORS OF FACILITIES FOR COLLECTION, RECEPTION, TREATMENT, STORAGE, TRANSPORT AND DISPOSAL OF HAZARDOUS WASTE UNDER THE HAZARDOUS & OTHER WASTES (MANAGEMENT & TRANSBOUNDARY MOVEMENT) RULES, 2016

M/s Green Valley Industries Limited of Village Nongsning, East Jaintia Hills District, Meghalaya is hereby granted / renewal of the Authorization to operate a facility for collection, storage and disposal of hazardous waste on its premises situated at Village Nongsning, East Jaintia Hills District, Meghalaya with reference to Application No. GVIL/MSPCB/HW/2021-22/05, Dtd: 28/01/2022.

The Authorization is granted / renewed to operate a facility for collection, storage and disposal of hazardous waste in accordance to the hazardous waste management matrix as specified below:-

HAZARDOUS AND OTHER WASTE MANAGEMENT MATRIX

	Hazardous Waste	Quantity	Collection	Reception	Treatment	Transport	Storage	Disposal
1	Used/ Spent Oil	29.79 KL/A	✓	X	X	X	✓ Leak proof containers	✓ Recycling within the plant premises Sale/auction to registered recycler/refiner

The Authorization shall be in force for a period of 5(five) years, i.e., from 1st February, 2022 upto 31st January, 2027.

The Authorization is subject to the conditions stated below and such conditions as may be specified in the Rules for the time being in force under the Environment (Protection) Act, 1986.

TERMS AND CONDITIONS:

1. The Authorization shall comply with the provisions of the Environment (Protection) Act and Rules made there under.
2. The Authorization shall be produced for inspection at the request of an officer authorized by the Meghalaya State Pollution Control Board.

Contact details: Email: members@megpcb.gov.in, megpcb@rediffmail.com; Telephone Numbers: Chairman-0364-2521717; Member Secretary-2472807; Scientific-2521514; Engineering-2521533; Legal-2520044; Laboratory-2521726; Administration-2520073; Accounts-2522104; Telcel-2521654.



Annexure-11



Meghalaya State Pollution Control Board
Forests & Environment Department, Government of Meghalaya
'ARDEN' Lumpyngngad, Shillong-793014
Website: <https://megspcb.gov.in>



No. MPCB/ATH-34/2011/2021-2022/23

Dated Shillong, the 7th Feb, 2022

FORM - 2 [See Rule 6(2)]

FORM FOR GRANT OF AUTHORIZATION BY MEGHALAYA STATE POLLUTION CONTROL BOARD, SHILLONG FOR OCCUPIERS, REPROCESSORS, REUSERS AND OPERATORS OF DISPOSAL FACILITIES FOR COLLECTION, RECEPTION, TREATMENT, STORAGE, TRANSPORT, DISPOSAL & CO-PROCESSING OF HAZARDOUS & OTHER WASTE UNDER THE HAZARDOUS & OTHER WASTE (MANAGEMENT & TRANSBOUNDARY MOVEMENT) RULES, 2016

M/s Green Valley Industries Limited of Village Nongsning, East Jaintia Hills District, Meghalaya is hereby granted of the Authorization to operate a facility for Collection, Reception, Storage & Co-Processing of Plastic Waste, Saw Dusts, Bamboo Chips, Tyre Chips and Rice Husk on its premises situated at Village Nongsning, East Jaintia Hills District, Meghalaya with reference to Application No. GVIL/MSPCB/HW/2021-22/06, Dtd: 28/01/2022.

The Authorization is granted to operate a facility for Collection, Reception, Storage & Co-Processing of Non-Hazardous Waste in accordance to the hazardous waste management matrix as specified below:-

WASTE MANAGEMENT MATRIX

Sl. No.	Non-Hazardous Waste	Quantity in Tonnes per Annum	Collection	Reception	Storage	Co-Processing
1.	Plastic Waste	6,000				
2.	Saw Dusts	3,000				
3.	Bamboo Chips	5,000	✓	✓	✓	✓
4.	Tyre Chips	10,000				
5.	Rice Husk	5,000				

The Authorization shall be in force for a period of 5 (five) years, upto 28th February 2027.

The Authorization is subject to the conditions stated below and such conditions as may be specified in the Rules for the time being in force under the Environment (Protection) Act, 1986.



Annexure-I



Recognised By

PCB, Assam & MSPCB, Meghalaya

Envirocon Building, L.O.C.L (AOD) New Market
P.O.: Dighoi, Dist.: Tinsukia, Assam - 786 171
Ph: 03781-264414, 813008687, 867003872
E-Mail: envirocon@rediffmail.com

ISO 9001:2015 Certified
ISO 14001:2015 Certified

Report No.: ENV/GVIL/25-26/AA-05/01

Date: 10/06/2025

Order No.: 3650000001

Date: 08/04/2024


Report Issued To: **GREEN VALLEY INDUSTRIES LIMITED**

Village: Nongseing, P.O.: Chiehrupai, P.S.: Khichriat, East Jaintia Hills, Meghalaya

AMBIENT AIR QUALITY TEST RESULTS

Sl. No.	LOCATION(M) - LINE (S) ¹	Date of Sampling	PM 2.5 ($\mu\text{g}/\text{m}^3$)	PM 10 ($\mu\text{g}/\text{m}^3$)	SO ₂ ($\mu\text{g}/\text{m}^3$)	NO _x ($\mu\text{g}/\text{m}^3$)
			50	100	88	80
01	Near Guest House	17.05.2025	21.7	41.5	<5.0	<6.0
02	Near DM Plot	17.05.2025	27.8	46.2	<5.0	<6.0
03	Sit. Colony	10.05.2025	26.4	44.2	<5.0	<6.0

Analysis Protocol: IS 5102



Checked By: Mr. Pankaj Barua, ENVIROCON

NOTE:

- Results reported are valid at the time of test under the prevailing conditions of measurement.
- Results refer only to the particular parameters tested.
- This test report shall not be reproduced except in full, without the written permission of ENVIROCON, L.O.C.L (AOD) New Market, Dighoi - 786172, Assam.

Core Services: Environmental Monitoring & Data Generation, EIA & EMP, Environmental Audit & Allied Environmental Management jobs
Associate Services: Certification by Competent Person (CIP), NDT, Hydraulic Testing, Chartered Engineer Services etc.



Annexure-II



Recognised By

PCB, Assam & MSPCB, Meghalaya

Envirocon Building, I.O.C.I (ROD) New Market
P.O.: Digboi, Dist.: Tinsukia, Assam - 786 171
Pin: 03751-284414, 9436008687, 9876828913
E-mail: envirocon@rediffmail.com

ISO-9001:2015 Certified
ISO 45001:2018 Certified

Report No: ENV/CVL/25-26/SE-05/03

Date: 10/06/2025

Order No: S600601004

Date: 13/04/2024

Report issued to: GREEN VALLEY INDUSTRIES LIMITED

Village: Nongoring, P.O: Chichirupi, P. S: Khliehnuar, East Jaintia Hills, Meghalaya

STACK EMISSION TEST RESULTS

01	Test Ref. No.	ENV/2023/SE-05/03		
02	Date of Sampling	17.05.2023		
03	Material of Construction	M.S.		
04	Stack/duct/dia	Coker E. S.P.		
06	Stack Gas Temperature (°C)	232		
07	Exit Velocity of Gas (m/sec)	7.6		
Analysis Results of Flue Gas				
Sl. No.	Parameter(s)	Result(s)	Unit(s)	Limit(s)
1.	Particulate Matter	25	mg/Nm ³	30
04	Sulphur Dioxide (as SO ₂)	NDL*	mg/Nm ³	700
05	Oxides of Nitrogen (as NO _x)	NDL*	mg/Nm ³	600

*NDL: Below Detection Level

Checked By: Mr. Panitaj Baroi, ENVIROCON

NOTE: 1. Results reported are valid to the date of analysis under the prevailing conditions of measurement.
2. Results refer only to the particular person(s) named.
3. This report shall not be used for any other purpose without the written permission of ENVIROCON, I.O.C.I (ROD) New Market, Digboi - 786171, Assam.

Core Services: Environmental Monitoring & Data Generation, EIA & EMP, Environmental Audit & Allied Environmental Management jobs
Associate Services: Certification by Competent Person (CIP), NDT, Hydraulic Testing, Chartered Engineer Services etc.



Annexure-III



Recognised By

PCB, Assam & MSPCB, Meghalaya

Envirocon Building, I.Q.C.L (AOD) New Market
P.O.: Digboi, Dist.: Tinsukia, Assam - 786 171
Ph: 93751-984414, 9435005557, 9876086672
E-mail: envirocon@gmail.com

ISO 9001:2015 Certified
ISO 14001:2015 Certified

Report No.: ENV/GVIL/25-26/N-05/01

Date : 07/06/2025

Order No.: 3600013004

Date : 30/03/2024

Report Issued To : **GREEN VALLEY INDUSTRIES LIMITED**

Village: Nongain, P.O. Chichruphi, P.S.: Chibhrist, East Jaintia Hills, Meghalaya

NOISE LEVEL MEASUREMENT RESULTS

Sl. No.	Location(s)	Date of Measurement	Day Time		Night Time	
			L_{eq} (dB-A)	Limit (dB-A)	L_{eq} (dB-A)	Limit (dB-A)
1	North Main Gate	17.05.2025	60.0	75	59.8	70
2	Staff Colony	17.05.2025	44.9	55	45.6	45



Checked by: Mr. Paritaj Barot, ENVIROCON

NOTE: 1. Results reported are valid at the time and place under the prevailing conditions of measurement.
2. Results refer only to the particular parameters tested.
3. Printed reports shall not be reproduced except in full, without the written permission of ENVIROCON, I.Q.C.L (AOD) New Market, Digboi - 786171, Assam.

Core Services: Environmental Monitoring & Data Generation, EIA & EMP, Environmental Audit & Allied Environmental Management jobs
Associate Services: Certification by Competent Person (CIP), HDT, Hydraulic Testing, Chartered Engineer Services etc.



Annexure-IV



Recognised By

PCB, Assam & MSPCB, Meghalaya

Envirocon Building, I.O.C.L (AOD) New Market

P.O.: Digboi, Dist.: Tinsukia, Assam - 786 171

Ph: 03751-264414, 9435008887, 8876028872

E-mail: envirocon@rediffmail.com

ISO 9001:2015 Certified

ISO 45001:2018 Certified

Report No.: ENV/GVIL/25-26/FE-07/01


Date : 07/07/2025

Report issued To: **GREEN VALLIEY INDUSTRIES LIMITED**

Village: Nongsring, P.O.: Chiehruphi, P. S.: Khliehriat, East Jaintia Hills, Meghalaya

PROCESS FUGITIVE EMISSION TEST RESULTS

Date	Location	Fugitive Emission Result for SPM ($\mu\text{g}/\text{m}^3$)	Limit ($\mu\text{g}/\text{m}^3$)
14.07.2025	Coal Handling Area (Near DM Plant)	694	2000
14.07.2025	Lime Stone Crusher Section	1908	5000



Checked By: Mr. Pankaj Baroi, ENVIROCON

NOTE:

1. Results reported are valid at the time of and under the prevailing conditions of measurement.
2. Results refer only to the particular parameters tested.
3. This test report shall not be reproduced except in full, without the written permission of ENVIROCON, I.O.C.L (AOD) New Market, Digboi - 786171, Assam.

Core Services: Environmental Monitoring & Data Generation, EIA & EMP, Environmental Audit & Allied Environmental Management jobs
Associate Services: Certification by Competent Person (CIF), NDT, Hydraulic Testing, Chartered Engineer Services etc.



Annexure-V



enviROCON

Recognised By

PCB, Assam & MSPCB, Meghalaya

Envirocon Building, I.O.C.L (AOD) New Market

P.O.: Digboi, Dist.: Tinsukia, Assam - 786 171

Ph: 03751-264414, 9435008657, 8676028672

E-mail: envirocon@rediffmail.com

ISO 9001:2015 Certified

ISO 45001:2018 Certified

Report No.: ENV/GVIL/25-26/FE-07/01


Date : 07/07/2025

Report issued To: **GREEN VALLIEY INDUSTRIES LIMITED**

Village: Nongsning, P.O.: Chiehruphi, P. S.: Khliehriat, East Jaintia Hills, Meghalaya

PROCESS FUGITIVE EMISSION TEST RESULTS

Date	Location	Fugitive Emission Result for SPM ($\mu\text{g}/\text{m}^3$)	Limit ($\mu\text{g}/\text{m}^3$)
14.07.2025	Coal Handling Area (Near DM Plant)	694	2000
14.07.2025	Lime Stone Crusher Section	1908	5000



Checked By: Mr. Pankaj Baroi, **ENVIROCON**

- NOTE:**
1. Results reported are valid at the time of and under the prevailing conditions of measurement.
 2. Results refer only to the particular parameters tested.
 3. This test report shall not be reproduced except in full, without the written permission of ENVIROCON, I.O.C.L. (AOD) New Market, Digboi - 786171, Assam.

Core Services: Environmental Monitoring & Data Generation, EIA & EMP, Environmental Audit & Allied Environmental Management jobs
Associate Services: Certification by Competent Person (CIF), NDT, Hydraulic Testing, Chartered Engineer Services etc.

